

REQUEST AUTHORIZATION FOR MAYOR AND FINANCE OFFICER TO SIGN PROFESSIONAL SERVICES AGREEMENT OR AMENDMENT

Date: December 7, 2007

Project Name & Number: Catron Boulevard Sanitary Sewer Main Extension,
Project No.: SS06-1635

CIP #: 50671

Project Description: Extension of a proposed 8-inch sanitary sewer main east along Catron Blvd. from just east of Nugget Gulch Road to Vineyard Lane for the Villaggio at Golden Eagle and for other developable property in the general vicinity. Engineering Services include evaluation of pipe slope, alignment, and drawing preparation. Construction is currently scheduled for summer of '07.

Consultant: Sperlich Consulting, Inc.

**Original
Contract Amount:** \$9,915.00

**Original
Contract Date:** 11/6/06

**Original
Completion Date:** NA

Amendment Number: Two

Amendment Description: During the design process geotechnical exploration encountered substantial amounts of rock along the original sanitary sewer alignment west of the Peace Officers building. For this reason the sanitary sewer alignment was moved to Golden Eagle Dr. Amendment Two provides additional design services for the sanitary sewer main along Golden Eagle Dr., geotechnical evaluations for Golden Eagle sewer, developing grading plans for along Golden Eagle Dr., and designing a storm sewer with inlet for Golden Eagle Dr.

Current Contract Amount: \$44,704.00

Current Completion Date: 5/15/2008 constr.

Change Requested: \$11,900.00

New Contract Amount: \$56,604.00

New Completion Date: 5/15/2008 Constr.

Funding Source This Request:

Amount	Dept.	Line Item	Comments
\$11,900.00	604-834	4223	Sewer funds Amendment Two amount
\$11,900.00	Total		

Agreement Review & Approvals

 Project Manager Date: 12/7/07	 Division Manager Date: 12/7/07	 Department Director Date: 12/7/07
 City Attorney Date: 12/7/07		

ROUTING INSTRUCTIONS

Route two originals of the Agreement for review and signatures.
 Finance Office - Retain one original
 Project Manager - Retain second original for delivery to Consultant
 cc: Public Works
 Engineering
 Project Manager

FINANCE OFFICE USE ONLY

(Note to Finance: Please write date of Agreement in appropriate space in the Agreement document)

	Date	Initials	Approved
Appropriation	12/7/07	JB	(Y) N
Cash Flow			Y N

**AMENDMENT NO. 2 TO OWNER-ENGINEER AGREEMENT BETWEEN
CITY OF RAPID CITY
AND
SPERLICH CONSULTING, INC.
FOR
CATRON BOULEVARD SANITARY SEWER MAIN EXTENSION
PROJECT NO.: SS06 1635 / CIP 50671**

1.0 BACKGROUND INFORMATION

- a. **Effective Date of Original Owner-Engineer Agreement:** 11-28-06
- b. **Effective Date of Amendment No. 1 of Owner-Engineer Agreement:** 5-10-07
- b. **Owner:** City of Rapid City, 300 Sixth Street, Rapid City, SD 57701
- c. **Engineer:** Sperlich Consulting, Inc., 821 Columbus Street, Suite 1, Rapid City, SD 57701
- d. **Project:** Catron Boulevard Sanitary Sewer Main Extension, Project No. SS06 1635 / CIP 50671

2.0 PURPOSE OF AMENDMENT

Amendment No. 2 dated this 6th day of December 2007, modifies the terms and conditions of the existing agreement between the City of Rapid City and Sperlich Consulting, Inc. for professional services related to the Catron Boulevard Sanitary Sewer Main Extension, Project No.: SS06 1635 / CIP 50671.

3.0 OVERVIEW OF SCOPE OF SERVICES

- a. Provide monetary compensation for a Revised Design Phase Scope of Services Including:
 - 1. Design of gravity sewer main along Golden Eagle Drive ROW
 - 2. Additional soil borings along the new alignment
 - 3. Topographic survey along the proposed sewer alignment
 - 4. Prepare grading plan for south side of Golden Eagle Drive ROW
 - 5. Design plans for storm sewer and inlets on Golden Eagle Drive.

4.0 SUPPLEMENTAL INFORMATION

- a. Exhibit "B" – Services Not Included
- b. Exhibit "C" – Effective Labor Rates

5.0 PAYMENT

Amendment No. 2 to the original Owner-Engineer Agreement shall be for a total contract amount of \$11,900.00. Billings will be sent on a monthly basis, at our standard hourly rates, as services are provided to the City. Additional services will not be provided or billed to the City of Rapid City unless a written request is received from the City of Rapid City for additional services, and adjustments are made to the contract amount.

For the additional services and modifications to the existing Owner-Engineer Agreement, the City of Rapid City shall pay Sperlich Consulting, Inc, the following:

Original Contract Amount:	\$9,915.00 (Nine Thousand Nine Hundred Fifteen Dollars)
Amendment No. 1:	\$34,789.00 (Thirty-Four Thousand Seven Hundred Eighty-Nine Dollars)
Amendment No. 2:	\$11,900.00 (Eleven Thousand Nine Hundred Dollars)

Amended Contract Amount: \$56,604.00 (Fifty-Six Thousand Six Hundred Four Dollars)

6.0 ACCEPTANCE**CITY OF RAPID CITY:****ACCEPTED:**

By: _____
 Title: Mayor
 Date: _____

ATTEST:

By: _____
 Title: Finance Officer
 Date: _____

REVIEWED BY:

By: Haley B. Weber
 Title: Project Manager
 Date: 12/13/07

ENGINEER:**ACCEPTED:**

By: [Signature]
 Title: President
 Date: 12-10-07

ATTEST:

By: Kale R. McHabe
 Title: Project Manager
 Date: 12-10-07

EXHIBIT "A"

SERVICES NOT INCLUDED

The following services are not included in our scope of services. These services may be added at the request of the City of Rapid City, upon receipt of a written amendment to the contract. Such amendment to the contract would require additional fees.

- 1.0 Preparation of Plats
- 2.0 Construction Staking
- 3.0 Payment for Advertisement for Bids
- 4.0 Financial or Accounting Counseling (i.e. bid bonds, performance bonds, etc.)
- 5.0 Legal Services
- 6.0 Auditing Services


EXHIBIT "B"

SPERLICH CONSULTING, INC.
HOURLY RATES AND REIMBURSABLE COSTS
2007

Principal - Design Engineer	\$ 75.00/hr.
Design Engineer	\$ 75.00/hr.
Registered Land Surveyor	\$ 65.00/hr.
Survey Crew Chief	\$ 60.00/hr.
Survey Assistant/Rodman	\$ 50.00/hr.
Field Technician	\$ 50.00/hr.
Design Tech I	\$ 45.00/hr.
Design Tech II	\$ 50.00/hr.
Clerical	\$ 35.00/hr.

EXHIBIT "A"

PW010208-07

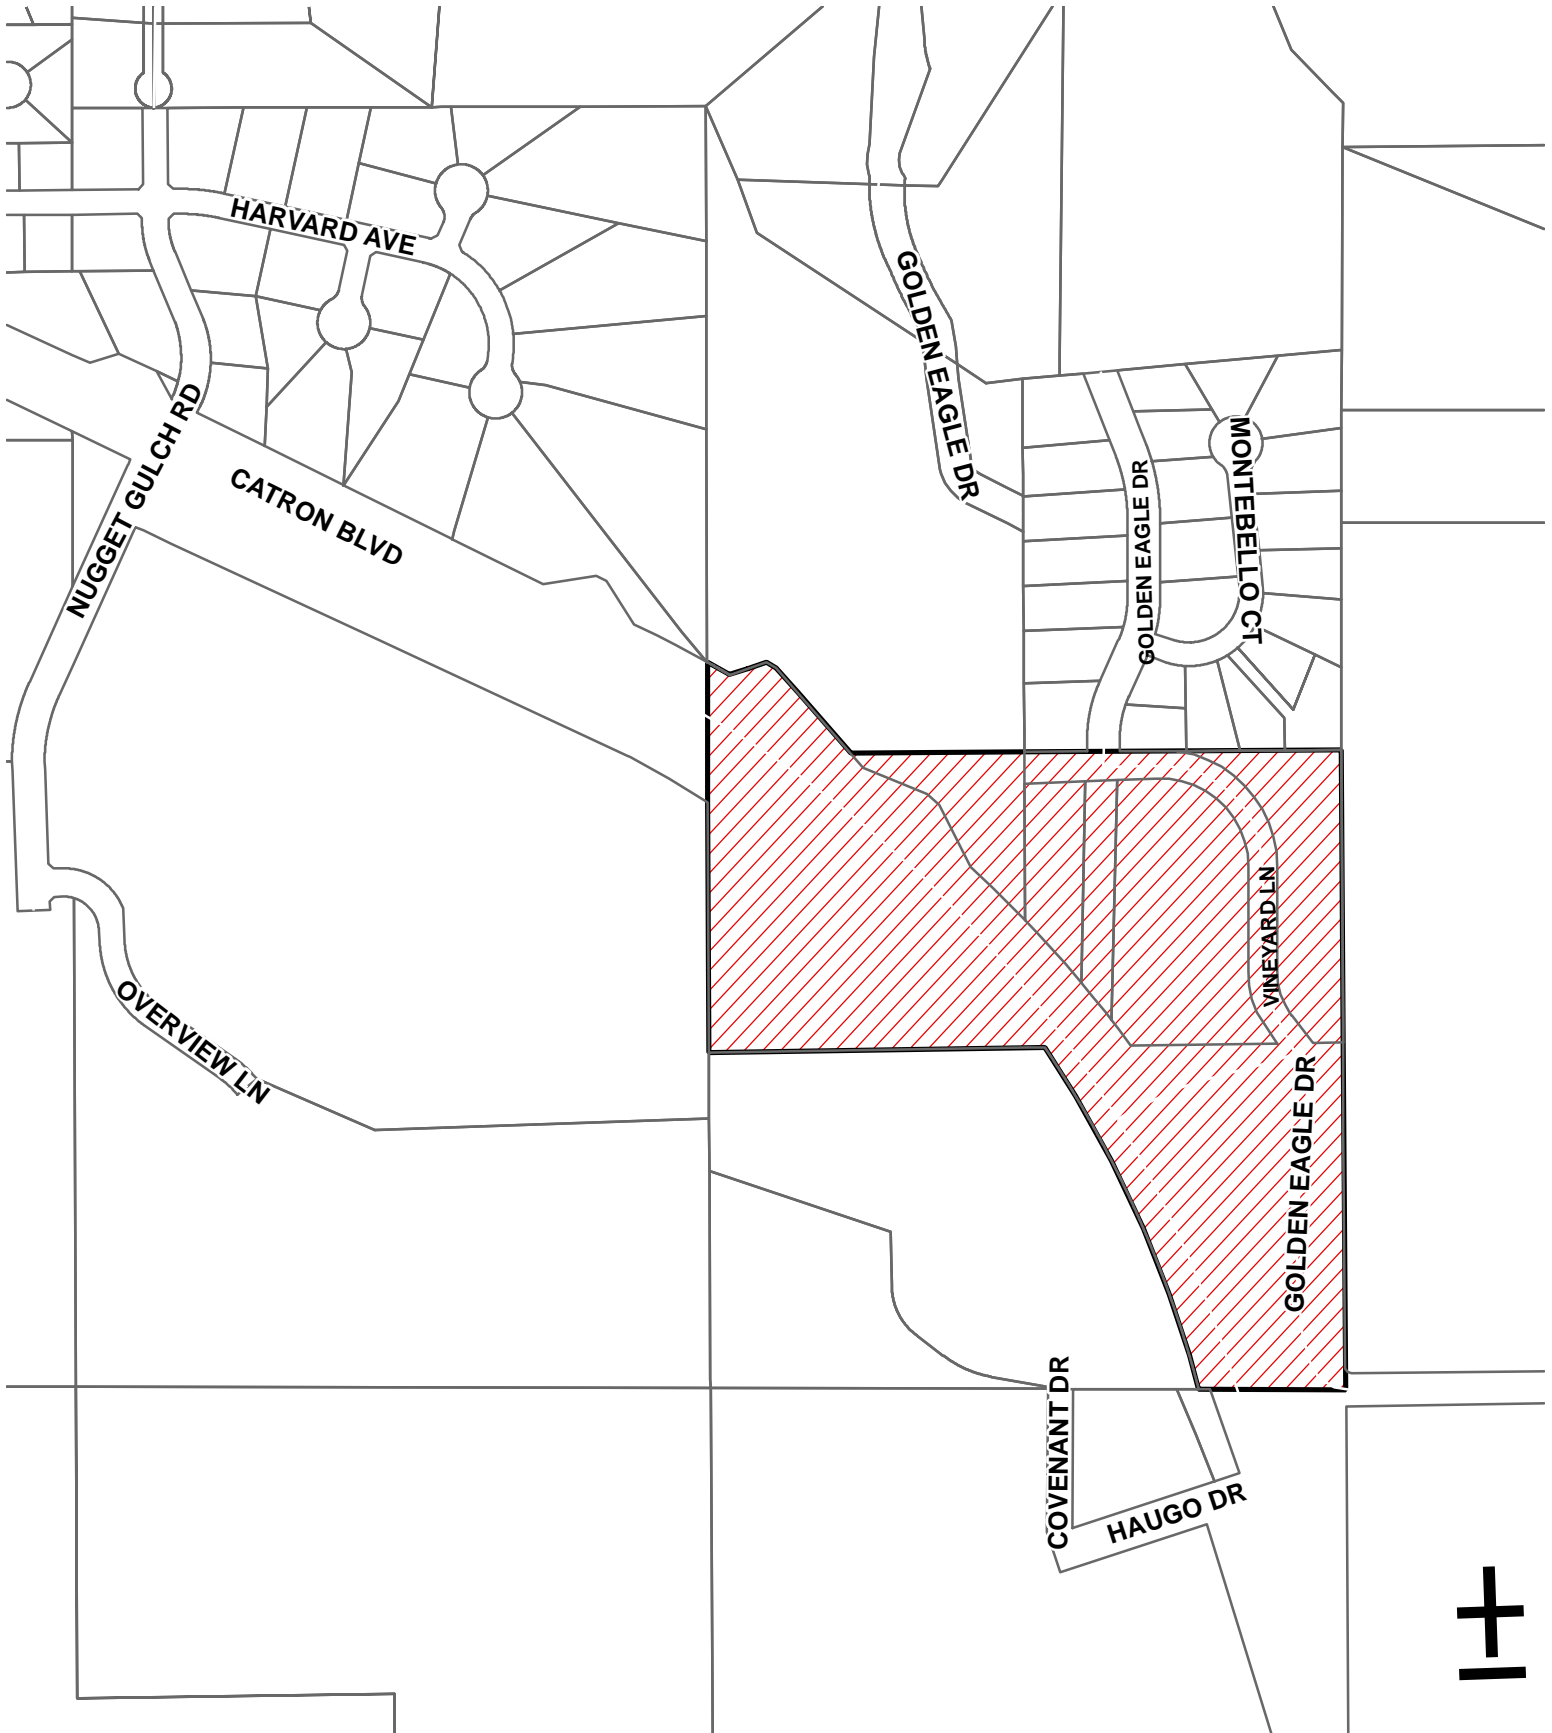

**CATRON BLVD SANITARY SEWER MAIN EXTENSION
PROJECT NO. SS06-1635 / CIP # 50671**
