

REQUEST AUTHORIZATION FOR MAYOR AND FINANCE OFFICER TO SIGN PROFESSIONAL SERVICES AGREEMENT OR AMENDMENT

Date:

Project Name & Number: Stoney Creek Water Booster Station and Well House,
Project No.: W03- 953

CIP #:
50318

Project Description: Combination Well House and Booster Station that provides water for the Hwy 16 elevated reservoir and the proposed Red Rock reservoir. Areas benefiting from the project are Hwy 16, Wildwood, Southwest, Carriage Hills, and Red Rocks.

Consultant: CETEC Engineering Services, Inc.

Original
Contract Amount: \$265,654.60

Original
Contract Date: October 09, 2006

Original
Completion Date: December
29, 2007

Addendum No: Two (2)

Amendment Description: Amendment is for the following services: 1. Provide supplemental construction observation and admin. services resulting from failure of Contractor to complete work within the specified contract time, 2. Provide additional services associated the City's two-year warranty period, and 3. Provide administrative and technical services associated with installation of a motorized control valve for surge control on booster pump discharge.

Current Contract Amount: \$290,992.10

Current Completion Date: December 26, 2008

Change Requested: \$18,205.51



New Contract Amount: \$309,197.61

New Completion Date: November 14, 2011

Funding Source This Request:

Amount	Dept.	Line Item	Fund	Comments
\$9,102.75	933	4223	602	Water Improvement
\$9,102.76	934	4223	602	Water Expansion
\$18,205.51	Total			

Agreement Review & Approvals

 4/21/10
Project Manager Date
 4/21/10
Compliance Specialist Date

Division Manager _____ Date

Department Director _____ Date

City Attorney _____ Date

ROUTING INSTRUCTIONS

Route two originals of the Agreement for review and signatures.
Finance Office - Retain one original
Project Manager - Retain second original for delivery to Consultant
cc: Public Works
Engineering
Project Manager

FINANCE OFFICE USE ONLY

(Note to Finance: Please write date of Agreement in appropriate space in the Agreement document)

Date _____ Initials _____ Approved _____
Appropriation _____
Cash Flow _____
Item #17

AMENDMENT NO. 2
TO
ENGINEERING SERVICES AGREEMENT

PROJECT: Well 12 and Stoney Creek Booster Station
City Project No. W03-953/CIP 50318

OWNER: City of Rapid City
Engineering Division
Attn: Stacey Titus, P.E., Project Manager
300 6th Street
Rapid City, SD 57701-2724

ENGINEER: CETEC Engineering Services, Inc.
1560 Concourse Drive
Rapid City, SD 57703

PURPOSE: This Amendment modifies terms and conditions of "*Standard Form of Agreement Between Owner and Engineer for Professional Services, Funding Agency Edition for Well 12 and Stoney Creek Booster Station, City Project No. W03-953/CIP 50318*" dated September 25, 2006. The terms and conditions of the referenced agreement shall remain unchanged unless specifically modified by this Amendment No. 2.

DATE: April 13, 2010

CHANGES TO AGREEMENT:

1. Provide supplemental construction observation and administrative services resulting from failure of Contractor to complete work during the specified contract time. Supplemental services include all labor and expenses for January 1, 2009 through December 31, 2009.
2. Provide additional services associated with evaluating and taking action on corrective or defective work covered by the Contractor's two-year warranty. Complete a two-year warranty inspection and report near the end of the warranty period.
3. Provide administrative and technical services associated with modification of booster pump discharge piping to include motorized surge control valve. Provide construction observation services. Assist with contractor price solicitation and negotiation. Provide necessary alterations to Operation and Maintenance Manual and as-built plans.

FEE ADJUSTMENT:

Amendment No. 2	
Item 1	\$13,605.51
Item 2	\$2,686.00
Item 3	\$1,914.00
Total Amendment No. 2	\$18,205.51

The adjusted maximum limiting fee, including this Amendment No. 2, shall be as follows:

Original Contract Amount			\$265,654.60
Amendment No. 1	October 8, 2008	+	\$25,337.50
This Amendment No. 2	April 13, 2010	+	<u>\$18,205.51</u>
Maximum Fee with Amendment No. 2			\$309,197.61

EXECUTION

In Witness whereof, the parties hereto have executed this Amendment No. 2 effective as of the latest date signed below.

OWNER

CITY OF RAPID CITY

By: _____

Title: Mayor

Date: _____

Attests: _____

Title: _____

By: _____

Title: Finance Officer

Date: _____

Attests: _____

Title: _____

Reviewed By: Steven J. Weber

Title: PROJECT MANAGER

Date: 4/21/10

Attests: _____

Title: _____

ENGINEER

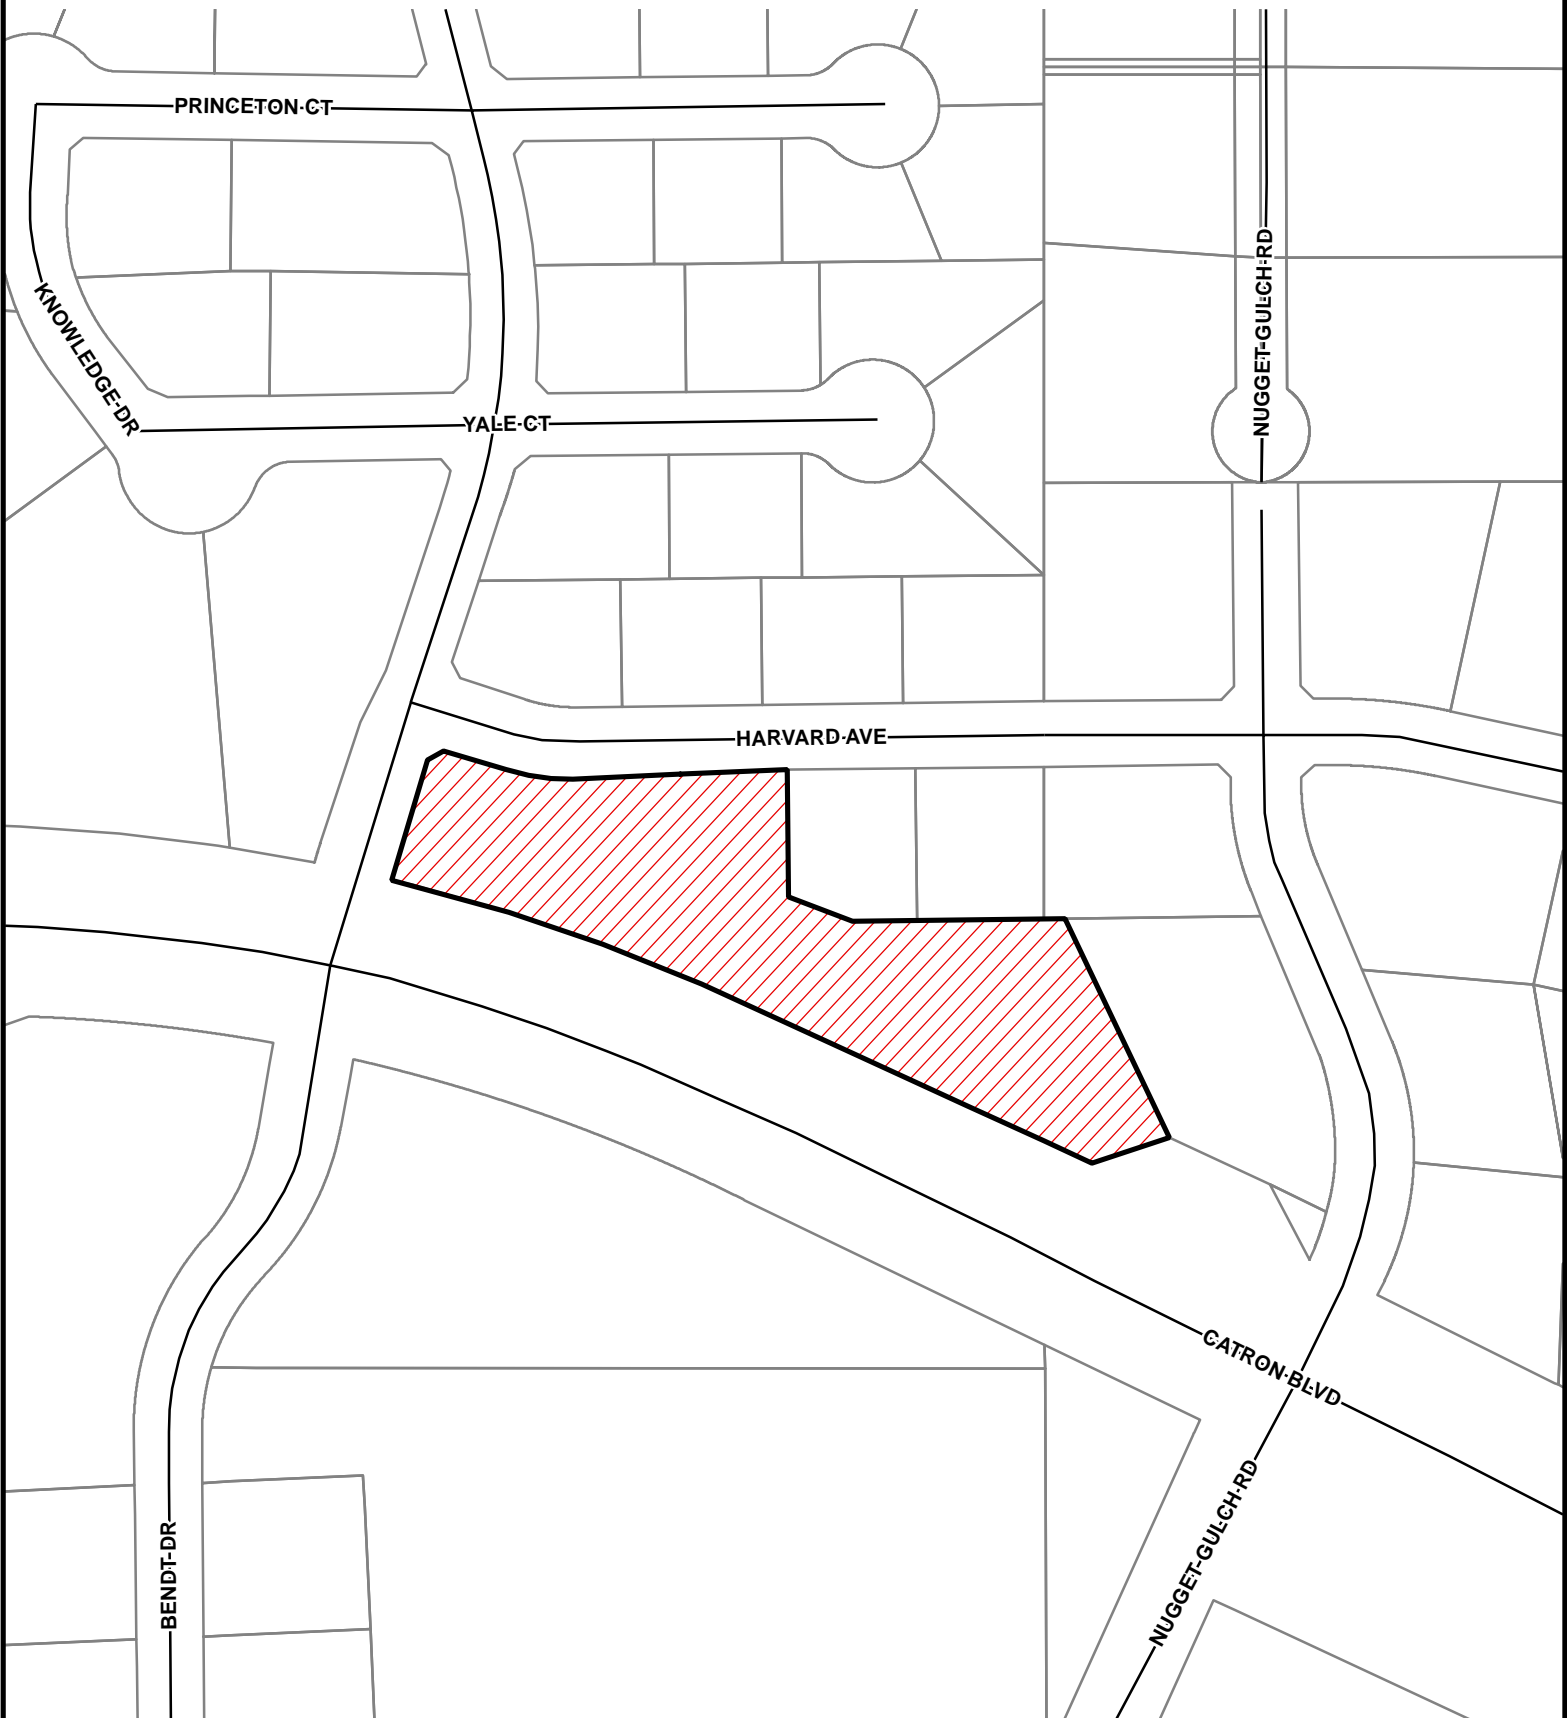
CETEC Engineering Services, Inc.

By: Theodore Schuff

Title: President

Date: 4/19/10

EXHIBIT "A"



WELL #12 STONEY CREEK BOOSTER STATION
PROJECT NO. W03-953
CIP 50318
