

REQUEST AUTHORIZATION FOR MAYOR AND FINANCE OFFICER TO SIGN PROFESSIONAL SERVICES AGREEMENT OR AMENDMENT

Date:

Project Name & Number: Red Rock Water Storage Reservoir, Project Number W02 - 1184

CIP #: 50284

Project Description: The City proposes construction of a 3.3 MG water storage reservoir in the Red Rocks Estates area. The reservoir will provide storage for a pressure zone similar to that of the HWY 16 elevated tank and pressure zone.

Consultant: "FourFront/enVision" and HDR Engineering, Inc.

Original Contract Amount: \$275,100

Original Completion Date: 10/6/03 design

Amendment Number: Two

Amendment Description: The Project construction duration is approximately two months longer than originally anticipated, additional work items were needed to address building permit and 11-6-19 review issues, and additional work was needed to address Pennington Co. landowner issues.

Current Contract Amount: \$367,323.00

Current Completion Date: 11/10/06 design

Change Requested: \$31,470.00

New Contract Amount: \$398,793.00

New Completion Date: 11/02/07 construction

Funding Source This Request:

Amount	Dept.	Line Item	Comments
\$31,470.00	934	4223	Water Enterprise
\$31,470.00	Total		

Agreement Review & Approvals

Project Manager Date

Division Manager Date

Department Director Date

City Attorney Date

ROUTING INSTRUCTIONS

Route **two** originals of the **Agreement** for review and signatures.
 Finance Office - Retain one original
 Project Manager - Retain second original for delivery to Consultant
 cc: Public Works
 Engineering
 Project Manager

FINANCE OFFICE USE ONLY

(Note to Finance: Please write date of Agreement in appropriate space in the Agreement document)

	Date	Initials	Approved	
Appropriation			Y	N
Cash Flow			Y	N

AMENDMENT NO. TWO TO OWNER-ENGINEER AGREEMENT

Red Rock Storage Reservoir - Project No. W03-1184

Subject of Amendment:
Extension of Construction Services and Owner Requested Additional Services

1. Background Data:

- a. Effective Date of OWNER-ENGINEER Agreement: April 21, 2003
- b. OWNER: City of Rapid City, South Dakota, 300 Sixth Street, Rapid City, SD 57701
- c. ENGINEER: enVision Design, Inc., 706 West Boulevard, Rapid City, SD 57701
- d. Project: Red Rock Storage Reservoir - Project No. W03-1184

2. Nature of Amendment

Change ENGINEER, in name only, from enVision Design, Inc. to **FourFront Design, Inc., 517 Seventh Street, Rapid City, SD 57701**

Additional Services to be performed by ENGINEER

Modifications to Completion Time for rendering Services

3. Description of Modifications


Attachment 1, "Modifications"

OWNER and ENGINEER hereby agree to modify the above-referenced Agreement as set forth in this Amendment. All provisions of the Agreement not modified by this or previous Amendments remain in effect. The Effective Date of this Amendment is _____.

CITY OF RAPID CITY:
ACCEPTED:

ENGINEER:

By: _____
Title: Mayor
Date Signed: _____


By: 
Title: President
Date Signed: 10/1/2007

ATTEST:

By: _____
Title: Finance Officer
Date Signed: _____

By: _____
Title: _____
Date Signed: _____

REVIEW BY:

By: 
Title: Project Manager
Date Signed: 9-27-07

This is **Attachment 1**, consisting of 1 page, to Amendment No. Two, dated _____.

Initial:

OWNER _____
ENGINEER _____

Modifications

A1. The Scope of Services currently authorized to be performed by ENGINEER in accordance with the Agreement and previous amendments, if any, is modified as follows:

1. To complete Out of Scope Work as follows:
 - a. Extension of Construction Services to the Contract Completion Date
 - b. Additional Progress Meetings
 - c. Dathe Property Grading Plan Revision
 - d. Building Permit / 11-6-19 Review Submittal and Approval

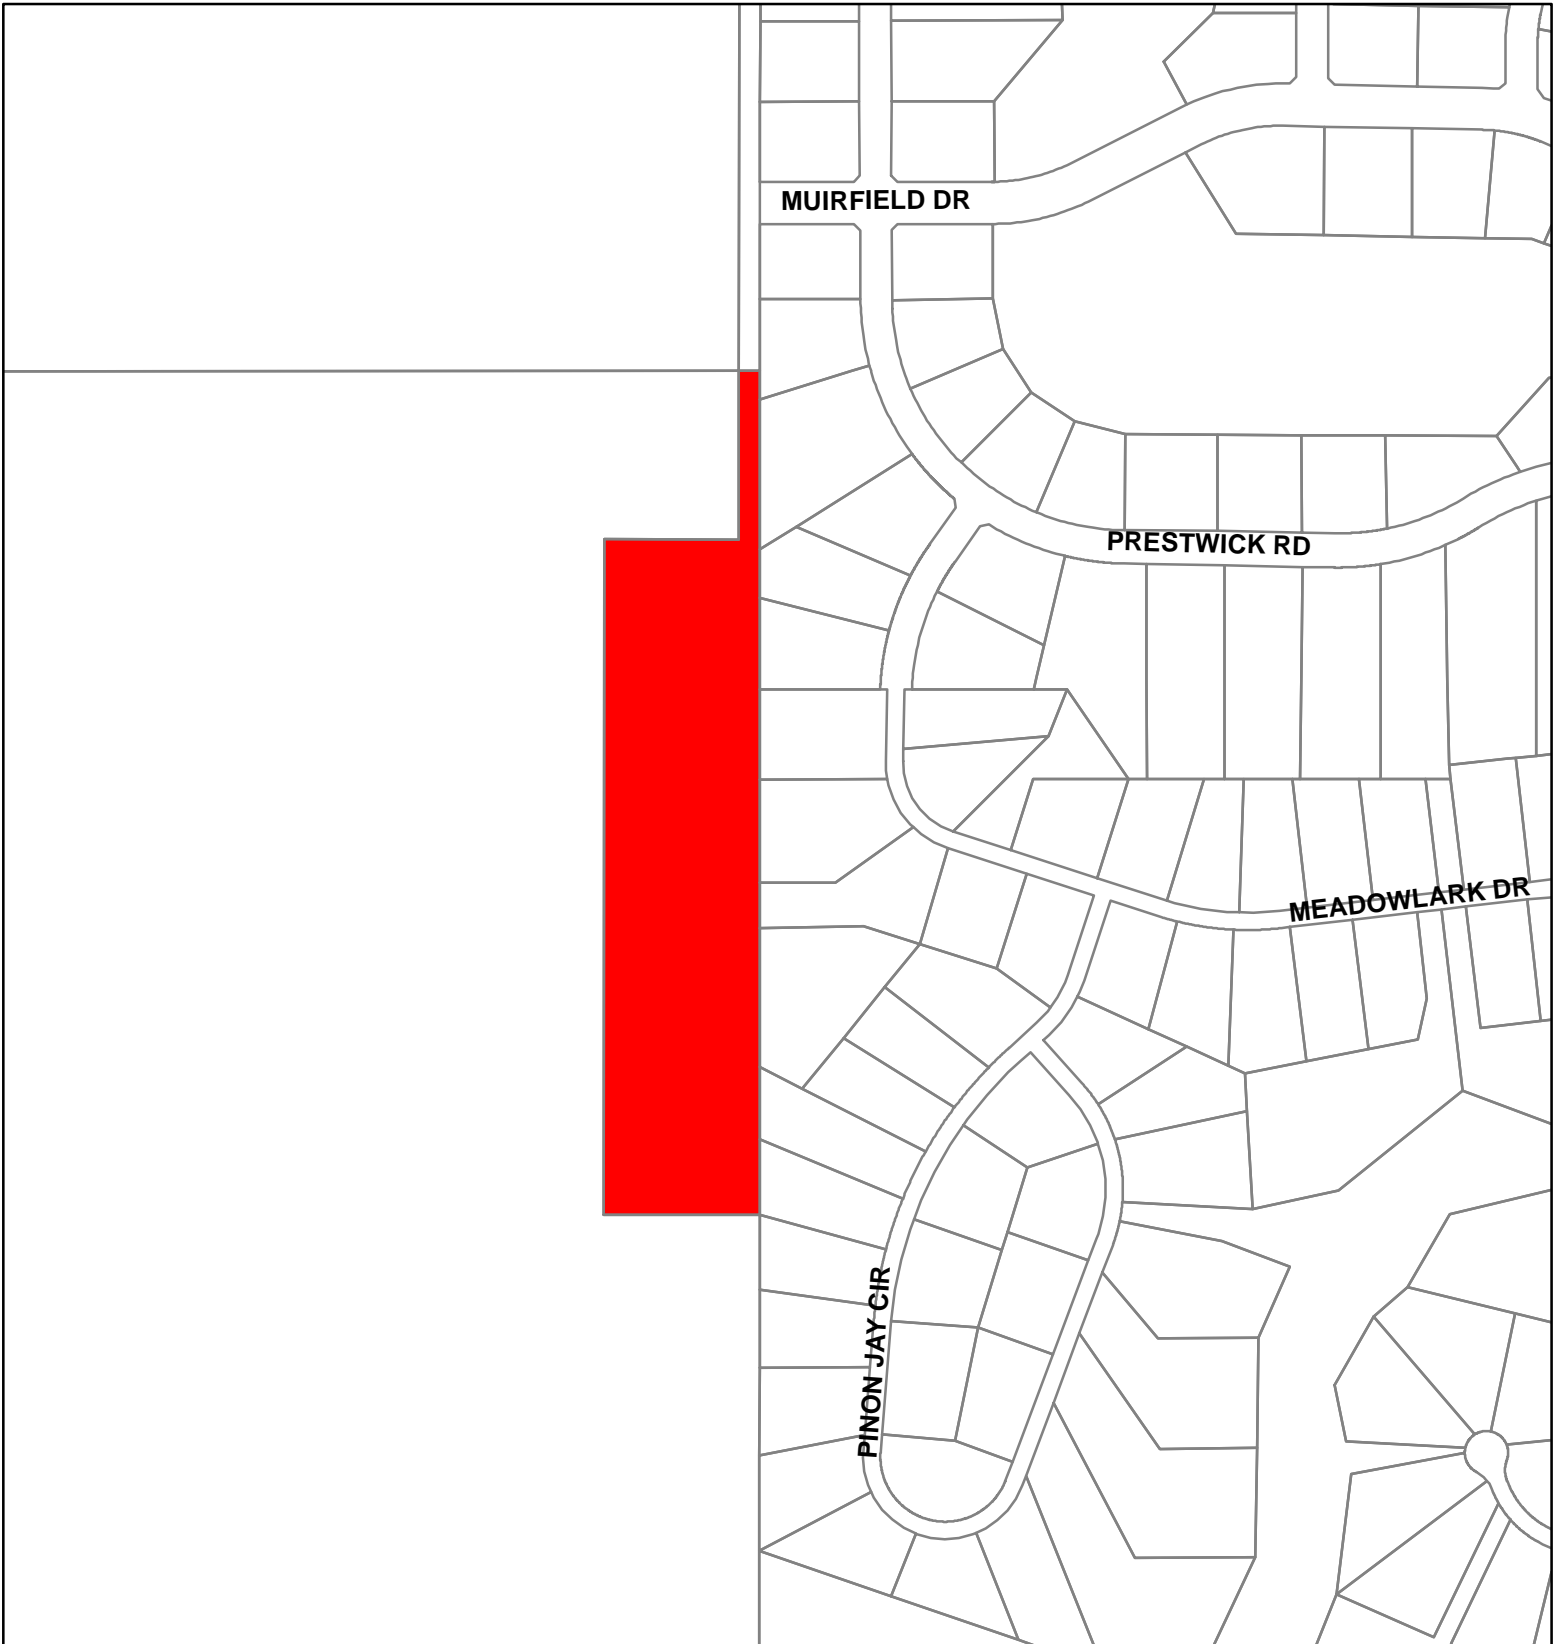
A2. For the Additional Services or the modifications to services set forth above, OWNER shall pay ENGINEER the following modified compensation:

Original Contract:	\$275,100 (Two Hundred Seventy-Five Thousand, One Hundred Dollars)
Revised Contract:	\$367,323 (Three Hundred Sixty-Seven Thousand, Three Hundred Twenty-Three Dollars)
Revised Contract: (This Addendum #2)	\$398,793 (Three Hundred Ninety-Eight Thousand, Seven Hundred Ninety-Three Dollars)
Increase of:	\$31,470 (Thirty-One Thousand, Four Hundred Seventy Dollars)

A3. The schedule for rendering services is modified as follows:

Construction Contract Completion by November 2, 2007

EXHIBIT "A"



**RED ROCK WATER STORAGE RESERVOIR
AMENDMENT NO. ONE
PROJECT NO. W02-1184
CIP # 50284**

