

# REQUEST AUTHORIZATION FOR MAYOR AND FINANCE OFFICER TO SIGN PROFESSIONAL SERVICES AGREEMENT OR AMENDMENT

**Date:**

Project Name &amp; Number: Red Rock Water Storage Reservoir, Project Number W02 - 1184

CIP #: 50284

**Project Description:** The City is constructing a 3.3 MG water storage reservoir in the Red Rocks Estates area. The reservoir will provide storage for a pressure zone similar to that of the HWY 16 elevated tank and pressure zone.

**Consultant:** "FourFront/enVision" and HDR Engineering, Inc.

**Original Contract Amount:** \$275,100

**Original Completion Date:** 10/6/03 design

**Amendment Number:** Three

**Amendment Description:** The Project construction duration is approximately seventeen weeks longer than originally contracted. Additional time and effort is required by the consultant to complete the project oversight as a result of this extended construction schedule.

**Current Contract Amount:** \$398,793.00

**Current Completion Date:** 11/02/07 construction

**Change Requested:** \$39,902.00

**New Contract Amount:** \$438,695.00

**New Completion Date:** 05/01/08 construction

**Funding Source This Request:**

Amount	Dept.	Line Item	Comments
\$39,902.00	934	4223	Water Enterprise
\$39,902.00	Total		

**Agreement Review & Approvals**

Project Manager \_\_\_\_\_ Date \_\_\_\_\_

Division Manager \_\_\_\_\_ Date \_\_\_\_\_

Department Director \_\_\_\_\_ Date \_\_\_\_\_

City Attorney \_\_\_\_\_ Date \_\_\_\_\_

**ROUTING INSTRUCTIONS**

Route **two** originals of the **Agreement** for review and signatures.  
 Finance Office - Retain one original  
 Project Manager - Retain second original for delivery to Consultant  
 cc: Public Works  
 Engineering  
 Project Manager

**FINANCE OFFICE USE ONLY**

(Note to Finance: Please write date of Agreement in appropriate space in the Agreement document)

	Date	Initials	Approved	
Appropriation			Y	N
Cash Flow			Y	N

**AMENDMENT NO. THREE TO OWNER-ENGINEER AGREEMENT****Red Rock Storage Reservoir – Project No. W03-1184****Subject of Amendment:  
Extension of Construction Services****1. Background Data:**

- a. Effective Date of OWNER-ENGINEER Agreement: April 21, 2003
- b. OWNER: City of Rapid City, South Dakota, 300 Sixth Street, Rapid City, SD 57701
- c. ENGINEER: FourFront Design, Inc, 517 Seventh Street, Rapid City, SD 57701
- d. Project: Red Rock Storage Reservoir – Project No. W03-1184

**2. Nature of Amendment**

Additional Services to be performed by ENGINEER

Modifications to Completion Time for Rendering Services

**3. Description of Modifications**

Attachment 1, "Modifications"

OWNER and ENGINEER hereby agree to modify the above-referenced Agreement as set forth in this Amendment. All provisions of the Agreement not modified by this or previous Amendments remain in effect. The Effective Date of this Amendment is \_\_\_\_\_.

CITY OF RAPID CITY:  
**ACCEPTED:**

By: \_\_\_\_\_  
Title: Mayor  
Date Signed: \_\_\_\_\_


**ATTEST:**


By: \_\_\_\_\_  
Title: Finance Officer  
Date Signed: \_\_\_\_\_

**REVIEW BY:**

By: \_\_\_\_\_  
Title: Project Manager  
Date Signed: \_\_\_\_\_

ENGINEER:

By:   
Title: President  
Date Signed: 1/9/08

By:   
Title: Engineering Dept Mgr.  
Date Signed: 1/9/08

This is **Attachment 1**, consisting of 1 page, to Amendment No. Three, dated \_\_\_\_\_.

Initial:

OWNER \_\_\_\_\_  
ENGINEER BSV

### Modifications

A1. The Scope of Services currently authorized to be performed by ENGINEER in accordance with the Agreement and previous amendments, if any, is modified as follows:

1. To complete Out of Scope Work as follows:

a. Extension of Construction Services from November 2, 2007 to May 1, 2008

A2. For the Additional Services or the modifications to services set forth above, OWNER shall pay ENGINEER the following modified compensation:

**Original Contract:** \$275,100 (Two Hundred Seventy-Five Thousand, One Hundred Dollars)

**Revised Contract:** \$398,793 (Three Hundred Ninety-Eight Thousand, Seven Hundred Ninety-Three Dollars)

**Revised Contract:** \$438,695 (Four Hundred Thirty-Eight Thousand, Six Hundred Ninety-Five Dollars)  
(This Addendum #3)

**Increase of:** \$39,902 (Thirty-Nine Thousand, Nine Hundred Two Dollars)

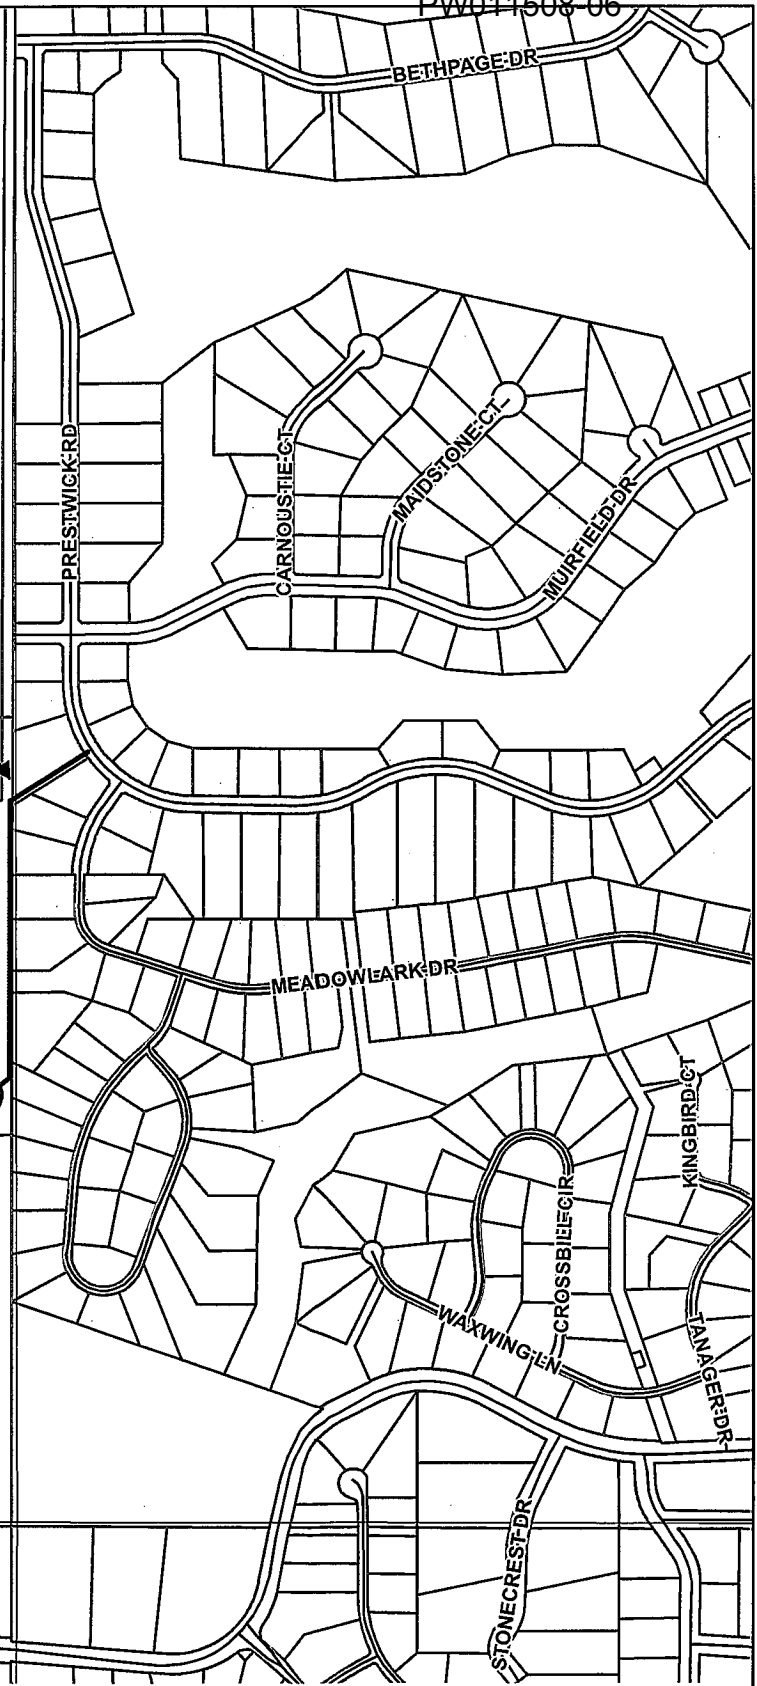
A3. The schedule for rendering services is modified as follows:

**Construction Contract Completion by May 1, 2008**



**WATER TRANSMISSION  
MAINS & RESERVOIR ACCESS**

**3.3 MILLION GALLON  
WATER STORAGE RESERVOIR**



**RED ROCK  
STORAGE RESERVOIR  
PROJECT NO. W03-1184**

3

**WATER TRANSMISSION  
MAINS & RESERVOIR ACCESS**

**3.3 MILLION GALLON  
WATER STORAGE RESERVOIR**

**RED ROCK  
STORAGE RESERVOIR  
PROJECT NO. W03-1184**

PW011508-06  
BETHPAGE-DR

PRESTWICK-DR

CARNOUSTIE-CT

MADSTONE-CT

MUIRFIELD-DR

MEADOWLARK-DR

KINGBIRD-CT

WAXWING-LN

CROSSBILL-CIR

TANAGER-DR

STONECREST-DR

SHERIDAN-LAKE-RD

ION-DR
