

REQUEST AUTHORIZATION FOR MAYOR AND FINANCE OFFICER TO SIGN PROFESSIONAL SERVICES AGREEMENT

Date: October 15, 2012

Project Name & Number: Canyon Lake Drive Reconstruction Project WTP10-878

CIP # 50004

Project Description: Construction Observation Services for the reconstruct of water mains, sanitary sewer mains, streets, and drainage improvements in Canyon Lake Drive between Jackson Boulevard and Soo San Drive.

Consultant: Ferber Engineering Company, Inc.

Original Contract Amount: \$612,710.00

Original Contract Date: 2/1/2011

Original Completion Date: 12/31/2012

Addendum No: 1

Amendment Description: Continued Construction Administration and Construction Observation services between scheduled completion date and actual completion date of construction of the project.

Current Contract Amount: \$612,710.00

Current Completion Date: December 31, 2012

Change Requested: \$49,720.00


New Contract Amount: \$662,430.00

New Completion Date:


Funding Source This Request:

Amount	Dept.	Line Item	Fund	Comments
\$6,463.60	833	4223	604	Sewer Enterprise Fund
\$6,463.60	933	4223	602	Water Enterprise Fund
\$36,792.80	932	4223	602	Bonds/SRF Loans
\$49,720.00	Total			

Agreement Review & Approvals




 Project Manager
 Date: 10/3/12




 Compliance Specialist
 Date: 10/3/12

 City Attorney
 Date: _____



 Division Manager
 Date: 10-3-12



 Department Director
 Date: 10-5-12

ROUTING INSTRUCTIONS

Route **two** originals of the **Agreement** for review and signatures.
 Finance Office - Retain one original
 Project Manager - Retain second original for delivery to Consultant
 cc: Public Works
 Engineering
 Project Manager

FINANCE OFFICE USE ONLY

(Note to Finance: Please write date of Agreement in appropriate space in the Agreement document)

Date	Initials	Approved
10/8/12		<input checked="" type="checkbox"/> Y <input type="checkbox"/> N
Cash Flow		<input type="checkbox"/> Y <input checked="" type="checkbox"/> N

AMENDMENT NO. 1 TO AGREEMENT

Project: Canyon Lake Drive Reconstruction
Project No. WTP10-878 / CIP No. 50004

Background Data: Original Contract Date: February 23, 2011
Owner: City of Rapid City, SD
Engineer: Ferber Engineering Company, Inc.

Nature of Amendment: Engineer continued to provide Construction Administration and Construction Observation Services during time between the scheduled completion date and actual completion date of construction of the project.

Current Contract Amount: \$612,710.00

Change Requested: \$49,720.00

New Contract Amount: \$662,430.00

Owner and Consultant hereby agree to modify the above referenced Agreement as set forth in this Amendment. All provisions of the Agreement not modified by this or previous Amendments remain in effect. The effective date of this Amendment is:

CITY OF RAPID CITY:

FERBER ENGINEERING
COMPANY, INC:

By: _____
Mayor

By: _____
President

Date: _____

Date: _____


ATTEST:

By: _____
Finance Officer

Date: _____

REVIEWED BY:

Project Manager

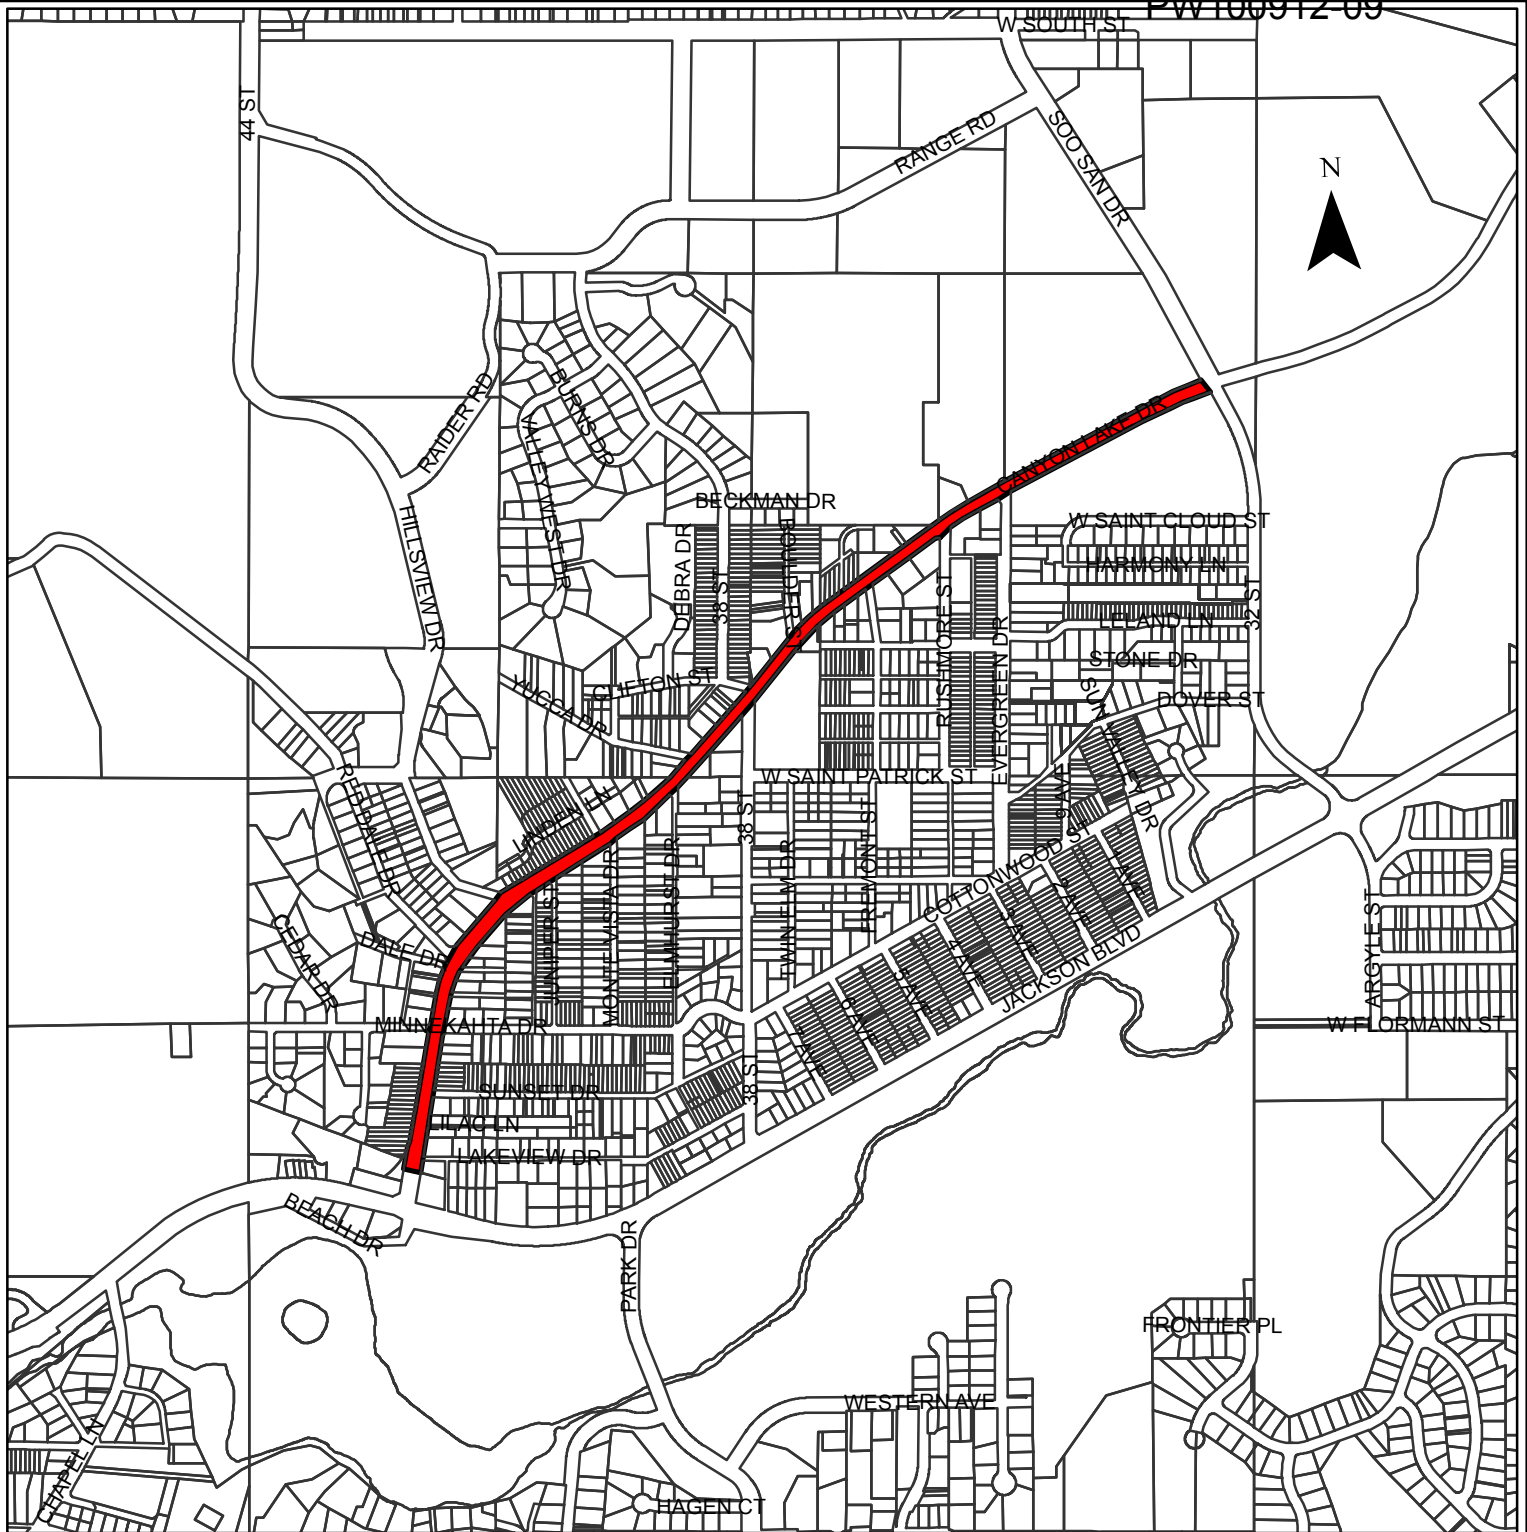

CANYON LAKE DRIVE RECONSTRUCTION PROJECT NO. WTP10-878 CIP NO. 50004

PROJECT IMPROVEMENTS

WATER MAINS, LAKEVIEW TO SOO SAN
 * 20" LOW PRESSURE MAIN
 * 12" HIGH PRESSURE MAIN

STORM SEWER, LAKE VIEW TO EVERGREEN
 * ADD/UPSIZE PIPES
 * INLETS

STANITARY SEWER MAINS, LAKEVIEW TO EVERGREEN
 * 8" MAINS & MANHOLES

STREET, LAKEVIEW TO EVERGREEN
 * 3 LANE STREET
 * BIKE PATH OR LANES
